



# Seafield Sludge Improvement Project - Stakeholder Update - January 2023


## Why are we here

- Update on progress of the project
- Agreed to tell you about key milestones
- Share update overall delivery timeline
- Key stakeholder engagement points

## Progress to date - Preparation/Planning stage

Item	Current status
Identify initial assets	✓
Scoping of the project	✓
Carry out outline design	✓
Review with Scottish Water	✓
Prepare packs for detailed design tendering process	✓
Commence Detailed design	✓
Engage with CEC Planning/SEPA	✓


# Recap on the main items to be delivered by the project

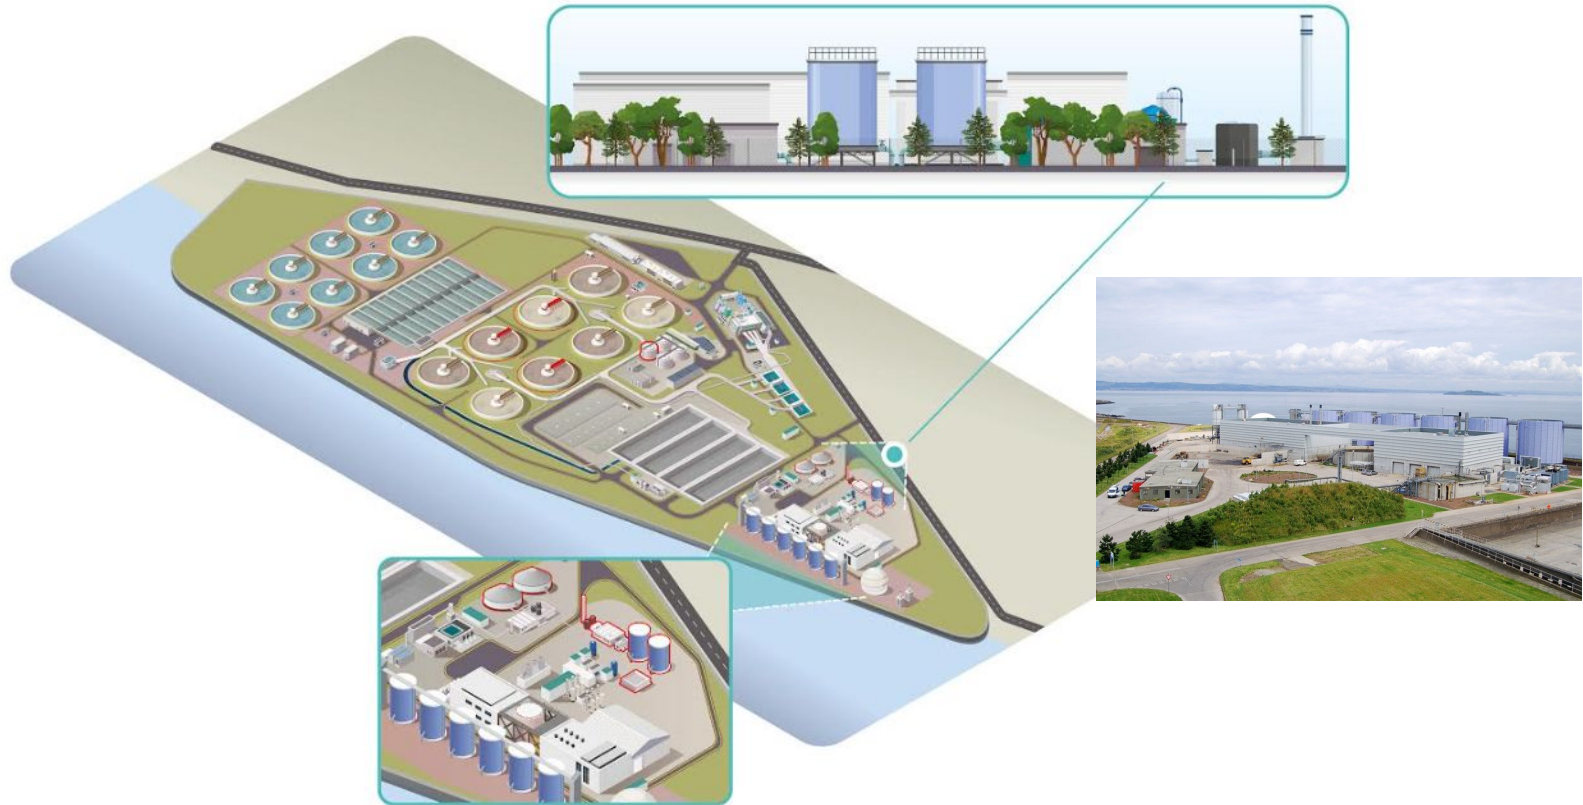

Currently going through pre planning discussions, planning application expected to be submitted by end of February, approval hoped for by end September

# Project Delivery - Timeline

## PROJECT TIMELINE

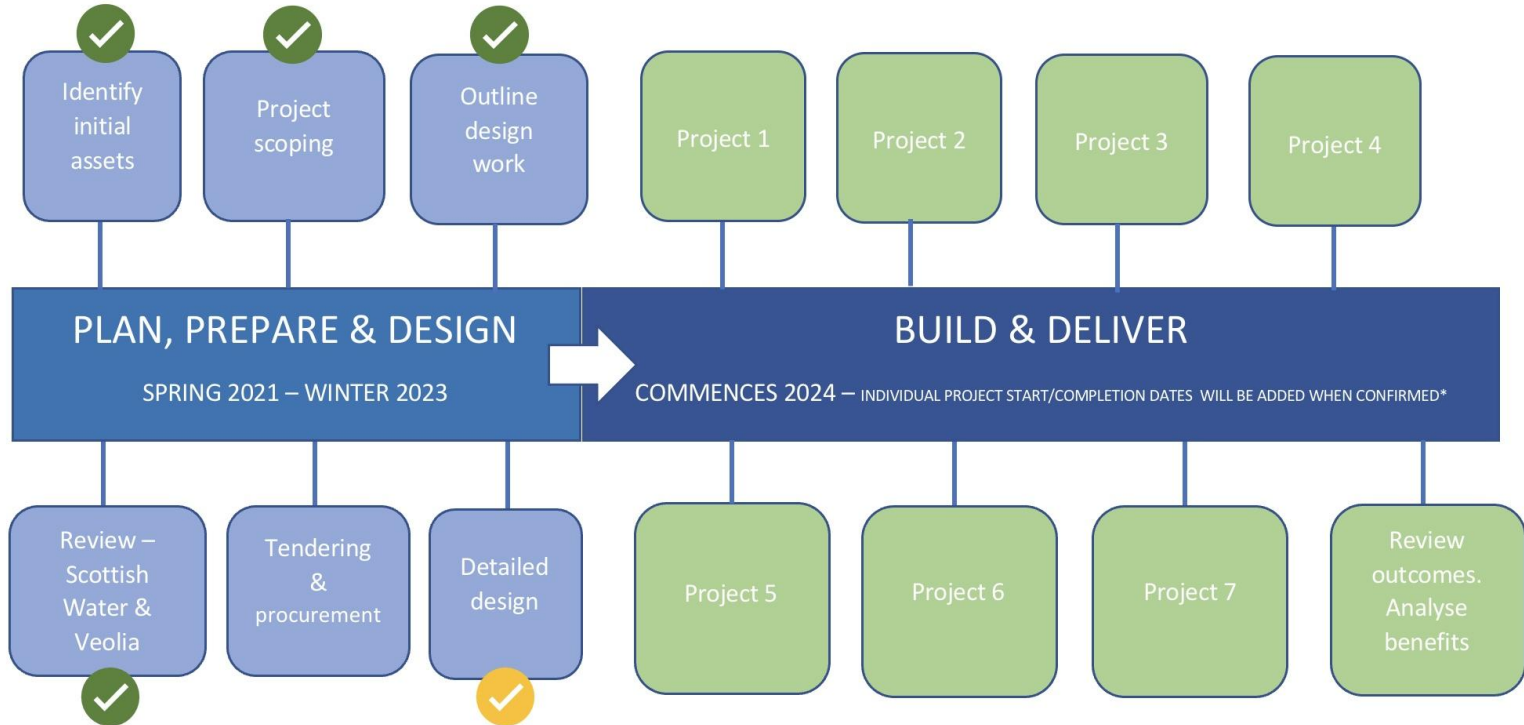

KEY: Complete In progress

\*Individual projects will be confirmed and added to timeline once detailed design phase has been completed.

# Stakeholder Engagement - Timeline

## **Consultation events**

March 2022 - Meetings with elected members, Leith Links Community Council, Leith Links Residents Association, Seafield Stakeholder Group Meeting

## **Public exhibition**

June 2022 - Public exhibition at Leith Links Gala Day  
September 2022 - General Public Doors Open Days  
October 2022 - Leith only Doors Open Days

## **Newsletter updates**

April and October 22 editions  
April and October 23 editions planned

## **Other updates**

January 2023 - Briefing for the City of Edinburgh Council

## **Future engagement**

Update on planning - Elected stakeholders (23rd Jan - 5th Feb)  
Neighbour notifications - February 2023  
Leith Gala Day - June 2023  
Leith residents/studio site visit - April 2023  
Periodic Newsletter updates  
Breaking ground event when construction work begins

*SEPA informed regularly through the monthly Environmental Liaison Group meetings*

